# Link Operations and Maintenance Facility: East

Citizen Oversight Panel

9/16/2020



# Link Operations & Maintenance Facility: East







#### Link OMF East

#### **Project Overview**

- Facility designed to service, deploy and store 96 LRVs – and maintain new mainline track, systems and stations
- Capacity of ~260 employees
- 24/7, 365 day operation
- Design-build project, fully furnished
- Supports operation of East Link, Lynnwood, Downtown Redmond and Federal Way Link Extensions

# Link OMF East - Financial Snapshot

Project Baseline Budget	\$449.2 million		
Committed	\$364.9 81%		
Incurred	\$343.8 77%		

Notes

~570,000 craft labor hours to-date

- 92% complete
- Contingency balance: 14.5% remaining
- Project baselined in July 2016, to be complete in December 2020

<sup>1.</sup> Year of Expenditure \$

<sup>2.</sup> Financials as of July 2020


#### Link OMF East - Workforce utilization

Apprent	tices	People	of Color	Wome	en	~570,000 craft labor hours
20.3%	20% goal	25%	15% goal	3.8%	9% goal	

Reported as of June 2020

Type	Design phase		Construction	
Small business enterprise	17.6%	12% goal	14.5%	12% goal
Disadvantaged business enterprise	6.3%	6% goal	12.2%	6% goal

 Design builder meets or exceeds contract specific and program-wide small and disadvantaged business or EEO goals except on gender

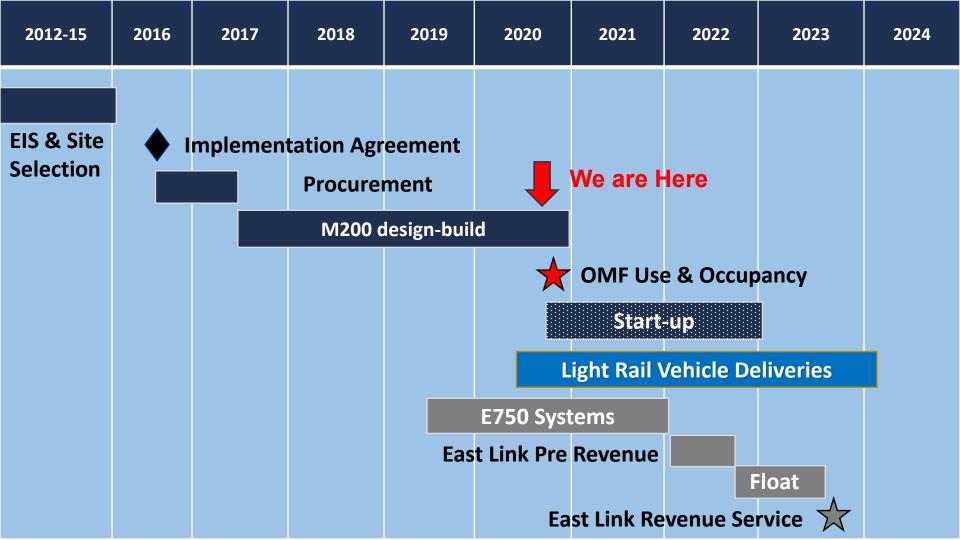

# Link OMF East - Remaining Work

#### Test and Commissioning phase

- In progress:
  - Installing equipment, building interior finishes
  - Commissioning systems such as heating/cooling, hoists, overhead power, switchgear
  - As-built Documentation


#### • Up next:

- Dynamic testing with light rail vehicles on-site
- Training maintenance personnel
- Asset management, verification and establishment of schedules for long-term care and custody of new facilities
- Hiring personnel including security and facility superintendents
- Substantially Complete by November 2020



# LRV storage yard nearing completion

OMF East has over 5 miles of track

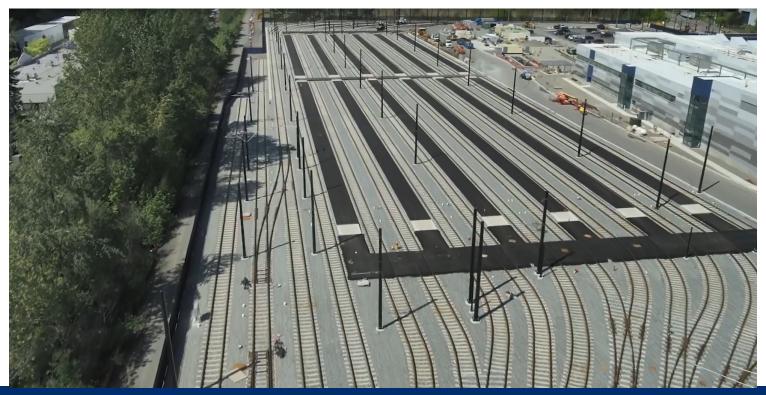

# LRV storage area nearing completion

Connection to East Link mainline – E335 contract






Vehicle monitoring, power, lighting, security systems and signs supported by ~ 300 poles across the 20-acre site




# Operation and Maintenance Facility (OMF)

144,700 Square feet of shops and offices

Leadership in Energy and Environmental Design - seeking Gold Certification

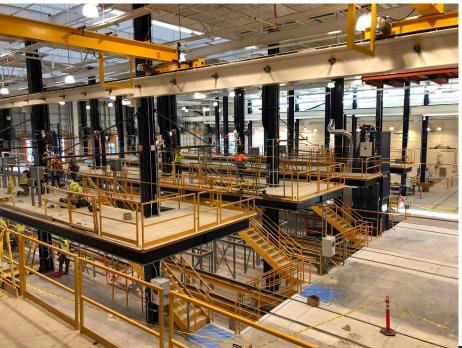

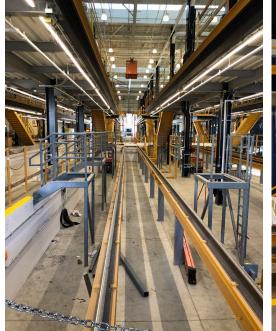



# The OMF Interior spaces

## Interior Finish – project is fully furnished at completion,

includes installation of over 1,300 individual items such as shelving, tools, equipment, and furniture











# Exterior View, South Entry, 120th Ave NE



## Exterior Finishes - Main Entrance





## **Exterior Finishes**






100 kw photovoltaic solar array on roof skylight monitors





# Maintenance of Way (MOW) Building

34,770 square feet of shops and offices

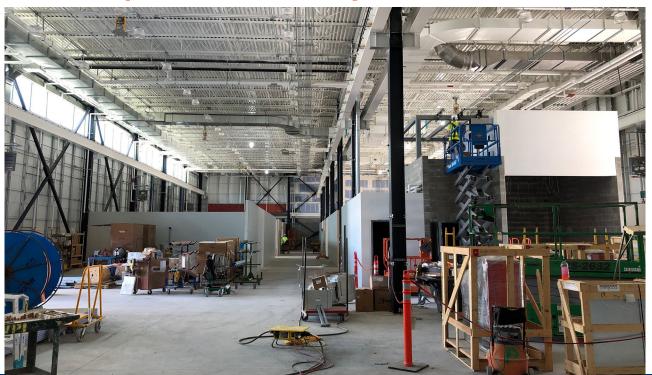

There are 7 overhead bridge cranes between the two buildings as well as 6 monorail hoists

# Facility Perimeter

#### Main Entrance along 120th AVE NE



#### Interim Bike Trail





# OMF East – Art Installation, Eastrail

"Nails", 478' long freestanding sculpture by Christian Moeller





# Light Rail Vehicle (LRV) Fleet Expansion

#### 21 of the 152 new LRVs ordered are in Seattle for testing

- Need to begin using OMF East yard capacity in Q1 2021
- LRV deliveries will continue into 2024









# Path to Project Acceptance

#### Risks and Challenges:

- COVID-19 Impacts
- Managing unforeseen issues that may arise during system testing
- Balancing need for Sound Transit human and fleet resources across multiple projects
- Implementing and testing changes made to support Series 2 LRVs
- Training staff, preparing for use and maintenance

### Next steps

Closeout property and utility easement actions with City of Bellevue	4 <sup>th</sup> Quarter 2020	
Substantial Completion & Certificate of Occupancy	November 2020	
Facility move-in ready	4 <sup>th</sup> Quarter 2020	
Tie-in to expanded mainline track and systems	2022	



# Thank you.



soundtransit.org





