East Link Extension Update

Motion Nos. M2023-21 through M2023-26


System Expansion Committee 03/09/2023



Why are we here

- Provide a status update on the East Link Extension and East Link Starter Line
- Inform today's decisions on six East Link contract/agreement motions.

East Link Alignment

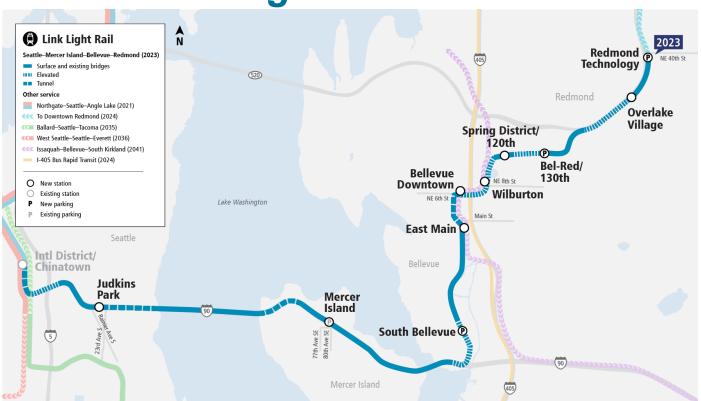

Redmond Technology Station Garage





Overlake Village, Bellevue Downtown Stations







Financial Snapshot


| Project Budget | \$3.677 B |
|----------------|-----------|
| Committed | \$3.329 B |
| Incurred | \$3.238 B |

- Year of Expenditure \$
- Financials as of January 2023


- 98.2% complete
- Project baselined in April 2015




East Link Starter Line

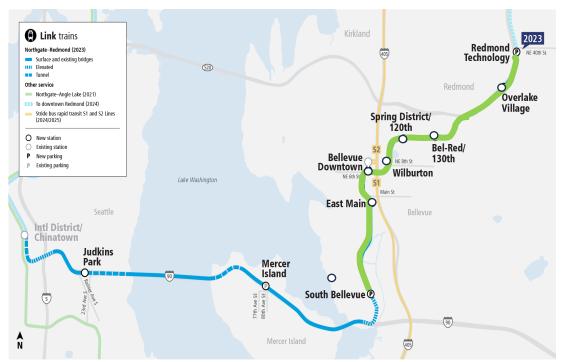



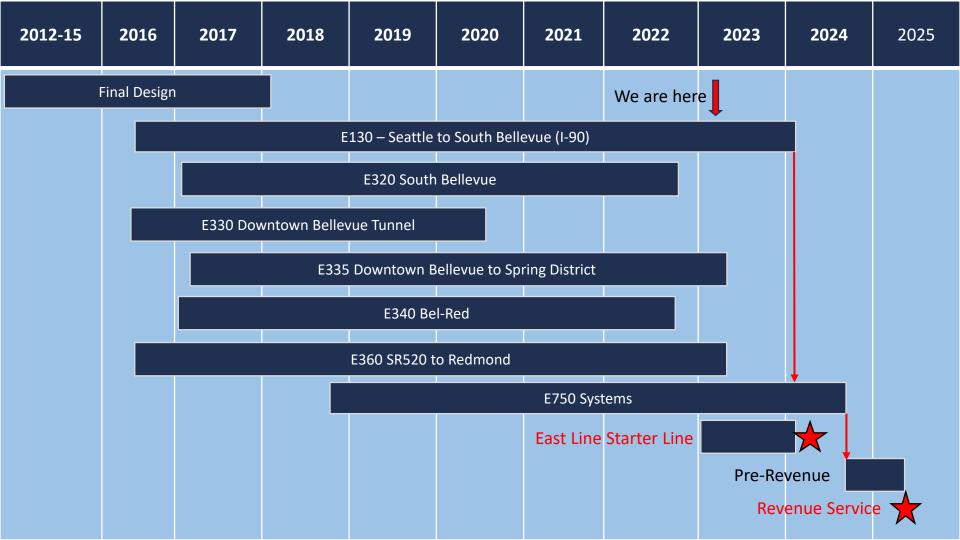


I-90 Track Plinth Reconstruction

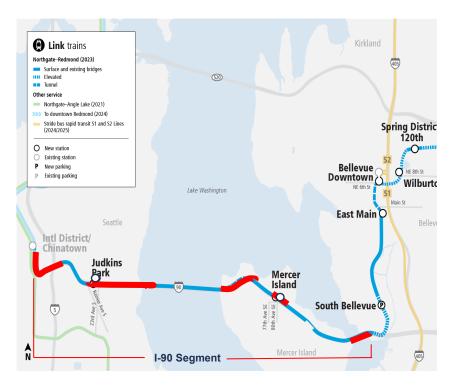



Track Plinth Reconstruction

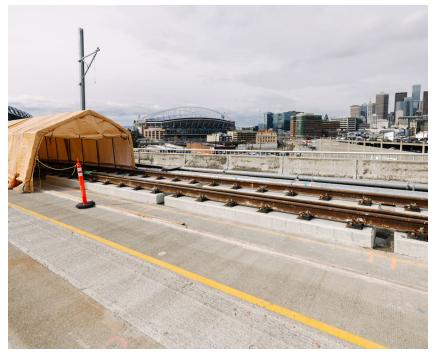




Today's Motions

- M2023-21 Amendment to Task Order B-11 with WSDOT for Construction Coordination of East Link Extension Overlake Segment
- M2023-22 Amendment to Task Order B-12 with WSDOT for Construction Coordination of the East Link I-90 Segment
- M2023-23 Contract Modification with Northwest Transit Systems Partners for the East Link Extension's Systems Construction Management Consultant Services
- M2023-24 Contract Modification with Mass Electric Construction Company for the East Link Extensions Systems Construction Contract
- M2023-25 Increase Contract contingency with Kiewit-Hoffman, East Link Constructors for the East Link Extension, Seattle to S Bellevue
- M2023-26 Contract Modification for East Link Extension I-90 Segment Construction Management Services



Motions M2023-21 & M2023-22 WSDOT

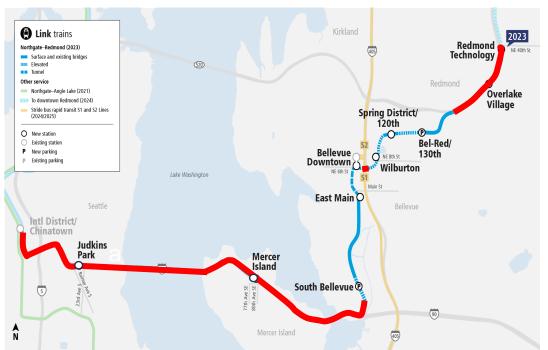



Motions M2023-23 and M2023-24






Motion M2023-25 Nylon Inserts





Motion M2023-26 I-90 Segment CMC

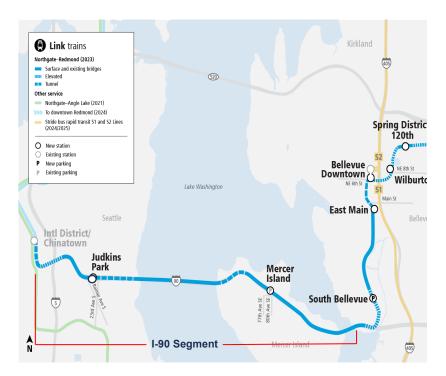




EAST LINK EXTENSION: Baseline Budget \$3.68B

Approve ___

ALLOCATION \$ COMMITMENTS

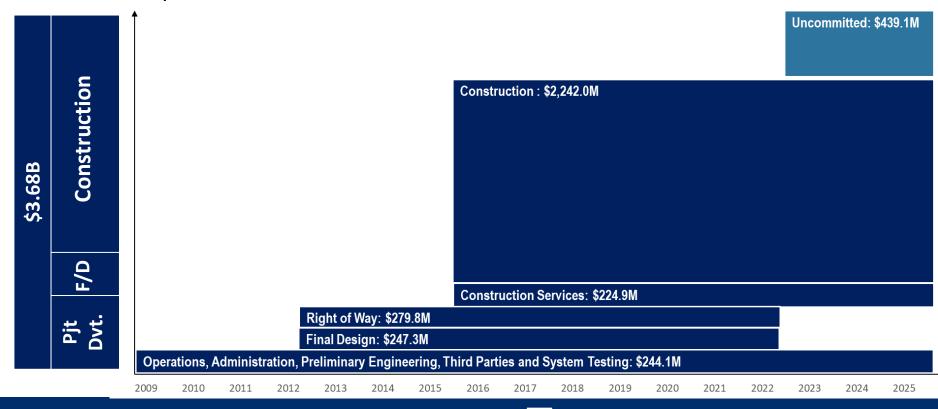


Today's

Future

SoundTransit

EAST LINK EXTENSION: Board Approves six motions for the following commitments ALLOCATION \$ COMMITMENTS

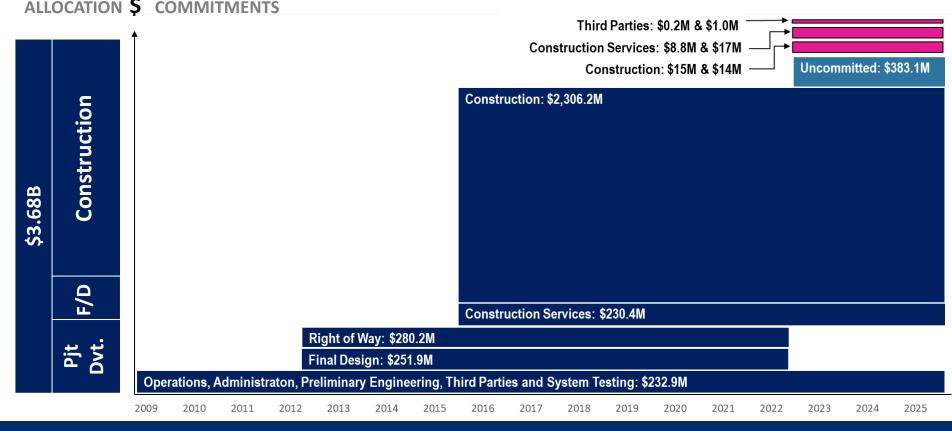










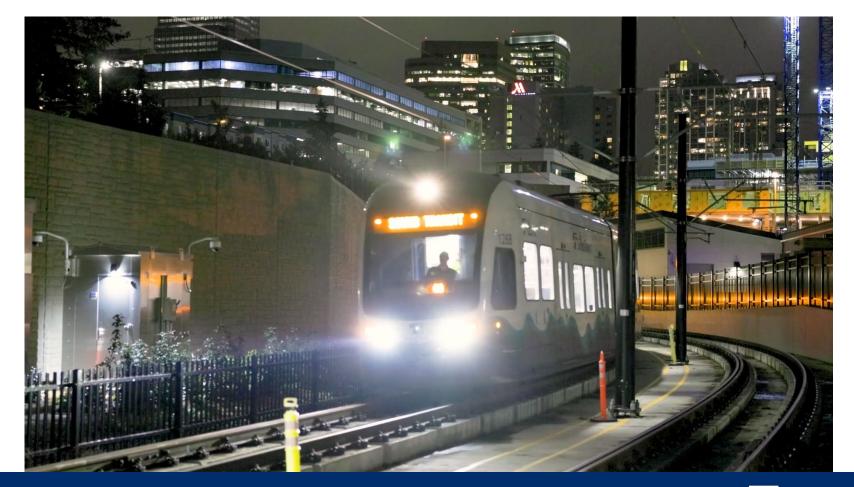



Thank you.



soundtransit.org





