East Link Extension Update

System Expansion Committee Meeting

11/10/2021



Why are we here


Project Status Update

- Redmond Technology Station Garage
- South Bellevue Garage Opening
- I-90 Segment


Motion No. M2021-67 - Construction Contract for the Mercer Island Transit Integration Project



East Link Alignment

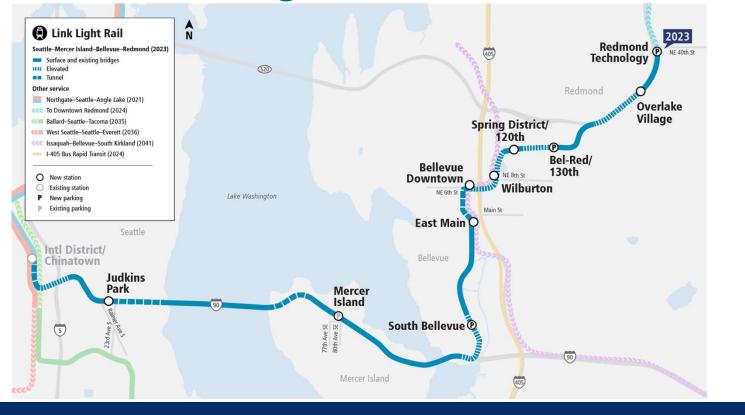



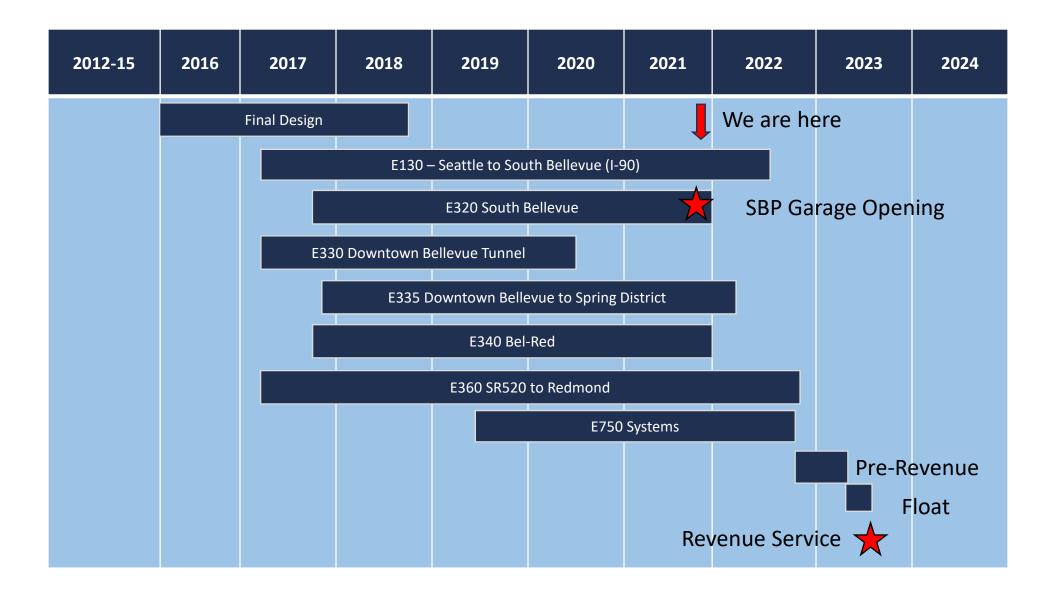

Financial Snapshot

Project Budget	\$3.677 B
Committed	\$3.194 B
Incurred	\$2.989 B
Year of Expenditure \$	

Financials as of September 2021

- 94% complete
- Project baselined in April 2015



Challenges / Upcoming Milestones

Challenges

- COVID-19 Impacts
- Station Schedules and Systems Access
- Redmond Technology Station Garage
- I-90 Segment Track Plinth Concrete Quality

Upcoming Milestones

- South Bellevue (E320) Garage Opening November 15, 2021
- South Bellevue (E320) Substantial Completion (Q4 2021)
- Bel-Red (E340) Substantial Completion (Q4 2021)
- Mercer Island Transit Integration Project– NTP (Q1 2022)



Redmond Technology Station Garage





Redmond Technology Station





Overlake Village Station





Bel-Red/130th Station





South Bellevue Station





South Bellevue Parking Garage






I-90 Floating Bridge








I-90 (E130) Track Plinth Concrete Quality

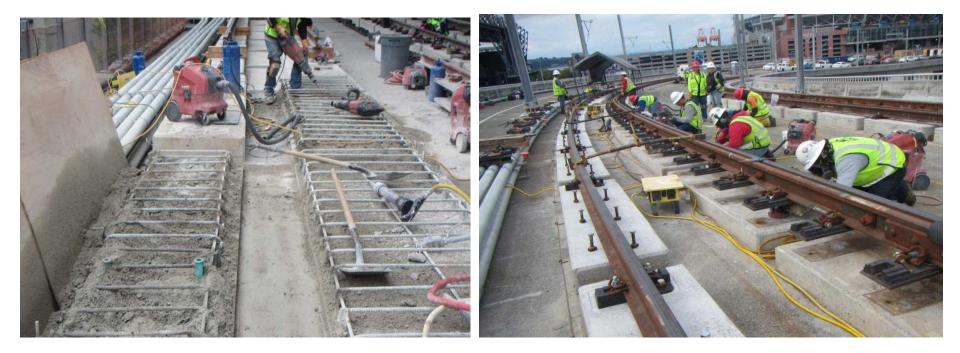



Judkins Park Station

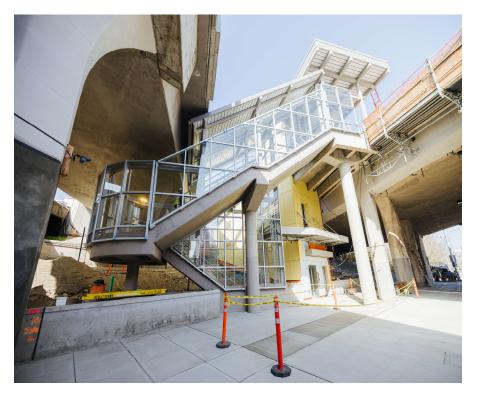






Today's Proposed Action

- Motion No. M2021-67 Construction Contract for the Mercer Island Transit Integration Project
 - Authorizes the chief executive officer to execute a contract with Johansen Construction Company for construction of the Mercer Island Transit Integration project as part of the East Link Extension in the amount of \$5,922,391, with a 15 percent contingency of \$890,000 for a total authorized contract amount not to exceed \$6,812,391.



Mercer Island Station



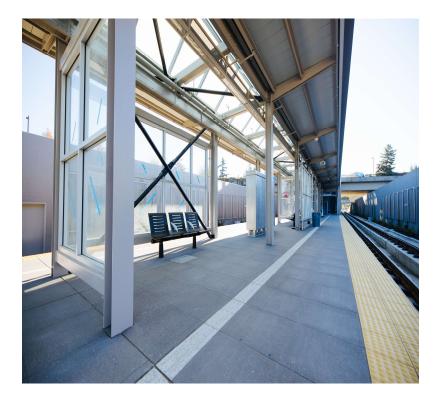



Mercer Island Transit Integration Project





Illustrative - Not to Scale

EAST LINK EXTENSION: Baseline Budget \$3.68B



Illustrative - Not to Scale

EAST LINK EXTENSION: Board Approves contract with Johansen Construction ALLOCATION \$ COMMITMENTS Company for \$6.8M in construction



Thank you.



soundtransit.org
f <> I
