

***Stride BRT Program
City of Bothell BAT Lanes Agreement
Amendment***

System Expansion Committee

03/10/22




Why we are here

- Construction update of City of Bothell Business Access and Transit (BAT) lanes project
- Seek authorization to extend the completion date of the City of Bothell delivered project, with no change in budget

SR 522 / NE 145th BRT: Project Overview

- 12 station pairs across 5 cities
- Connects Shoreline South/148th LRT Station, I-405 BRT (S2 Line), and the regional transit system
- 9 mile corridor
- High frequency service, 7 days a week
- Daily ridership ~ 8,900 in 2042
- 30 minutes: UW Bothell/Cascadia to Shoreline South/ 148th Station
- ST Express connection to Woodinville

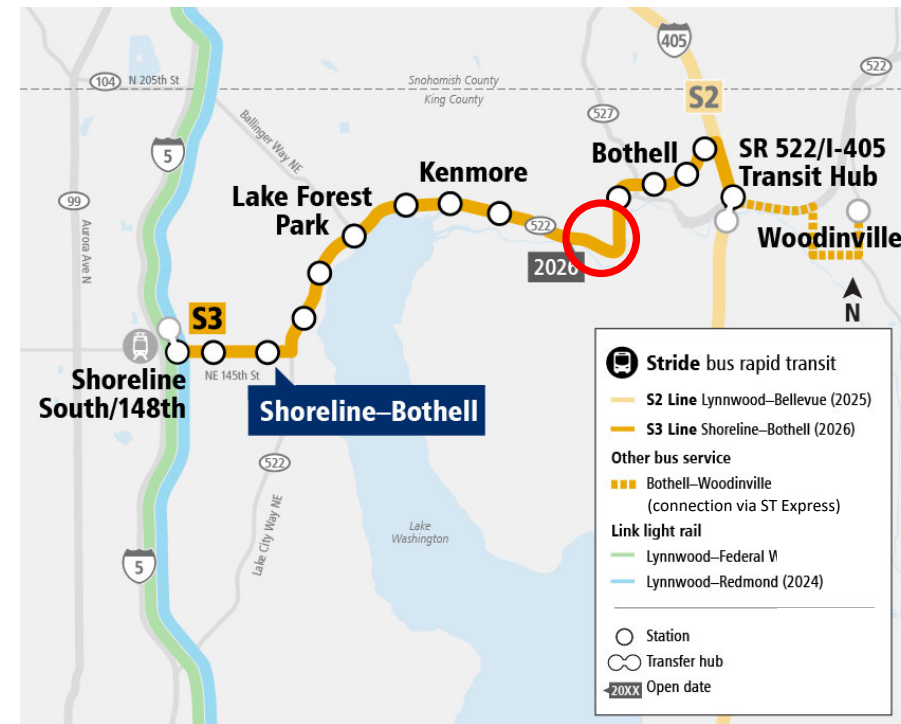

City of Bothell BAT Lanes Construction Agreement

- The 2019 agreement authorized \$24.9M over 36-months for City of Bothell to deliver 6400-ft of Business Access and Transit (BAT) lanes; including widening general purpose lanes, signal work, sidewalks, center medians, curb and gutter, retaining walls, street lighting, and landscaping.
- An agreement extension is required due to weather delays, adjacent third party utility work, pandemic-related impacts and required contract changes.
- Work is within budget and complete with the exception of final striping, completion of 12-month plant establishment period and punchlist items.

City of Bothell BAT Lanes Construction



SR 522 between 96th Ave NE and 83rd PI NE (Looking West)



North side of the SR 522, just east of 83rd PI NE (Looking East)

City of Bothell BAT Lanes Construction



South side of the SR 522, Burke-Gilman Trail just east of 83rd PI NE
(Looking East)



North side of SR 522 between 91st Ave NE and 83rd PI NE
(Looking West)

Today's proposed action

- Authorize the chief executive officer to amend an agreement with the City of Bothell to provide construction and construction management services for City of Bothell's Business Access and Transit (BAT) Lanes component of the SR-522/NE 145th BRT project to increase the time allowed to complete the project from 36 months to 52 months, with no change to the agreement amount.

Thank you.



 *soundtransit.org*

