
# Federal Way Link Extension Community Oversight Panel Briefing

*Community Oversight Panel 4/10/24* 



## What we'll cover today...

- FWLE Overview and community outreach
- Construction Status
- Schedule & Budget

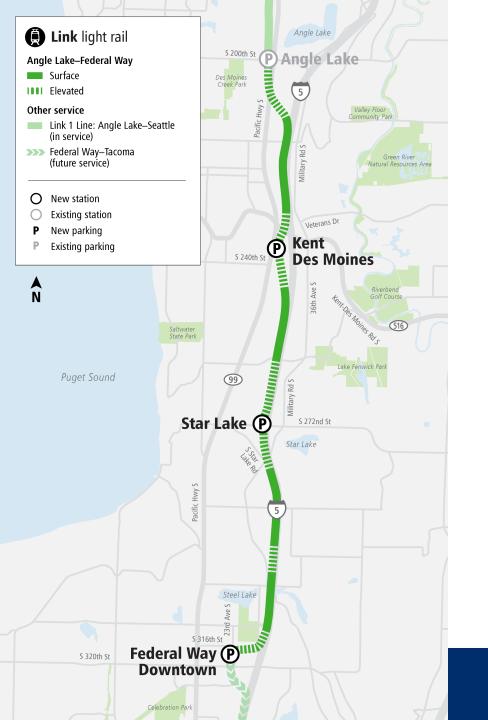

## Federal Way Link Extension (1 Line)

Angle Lake to Federal Way

- Length: 7.8 miles
- Stations: 3
  - Kent Des Moines, Star Lake and Federal Way Downtown stations (+3 parking garages)
  - ~3200 parking spaces
- Future transit-oriented development: KDMS (4 acres) and FWDS (6 acres)



## **FWLE Project Flyover Video**





## Placeholder for schedule and budget

Project Budget	\$2,451.5M	Milestone #	Description	Date
Committed	\$2,071.4M	4b	Complete Civil Work in WSDOT ROW	01-Nov- 24
Incurred\$1,830.6MNote: Financials as of February 2024. Project Baselined September 2018		5a	Substantial Completion of Work North of Structure C	05-Aug- 24
		5b	Substantial Completion of Work South of Structure C	31-Dec- 24
		5c	Substantial Completion of All Work	20-Nov- 25
		5d	Acceptance of All Work	20-Jan- 26
			Revenue Service Date	TBD



#### **Kent Des Moines Station**



**Substantial Completion: August 2024** 



#### **Star Lake Station**



#### **Substantial Completion: December 2024**



#### Federal Way Downtown Station



#### **Substantial Completion: December 2024**









#### Substantial Completion: December 2024 for civil work




### Angle Lake Tie-in



#### Scheduled: May 12 – June 23, 2024



## **Angle Lake Tie-in**

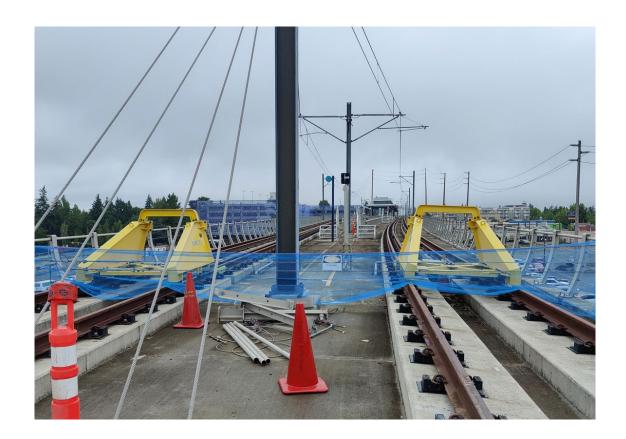

- Several OCS tie-in plans were evaluated
- As much work as possible is being done overnight
- The project is working with ST PIPP, Passenger Experience and Community Engagement, Safety and Operations



### Angle Lake Tie-in



•Angle Lake Station will be closed for certain hours for 3 weekends


•Single tracking will occur during the weekdays between these weekends

•Additional ST Ambassadors

•Additional buses (Bus Bridging) will be provided by the Rapid Ride A Line











soundtransit.org
f J O
