


# *East Link Extension*

## *System Expansion Committee Meeting*

04/14/2022



# East Link Alignment

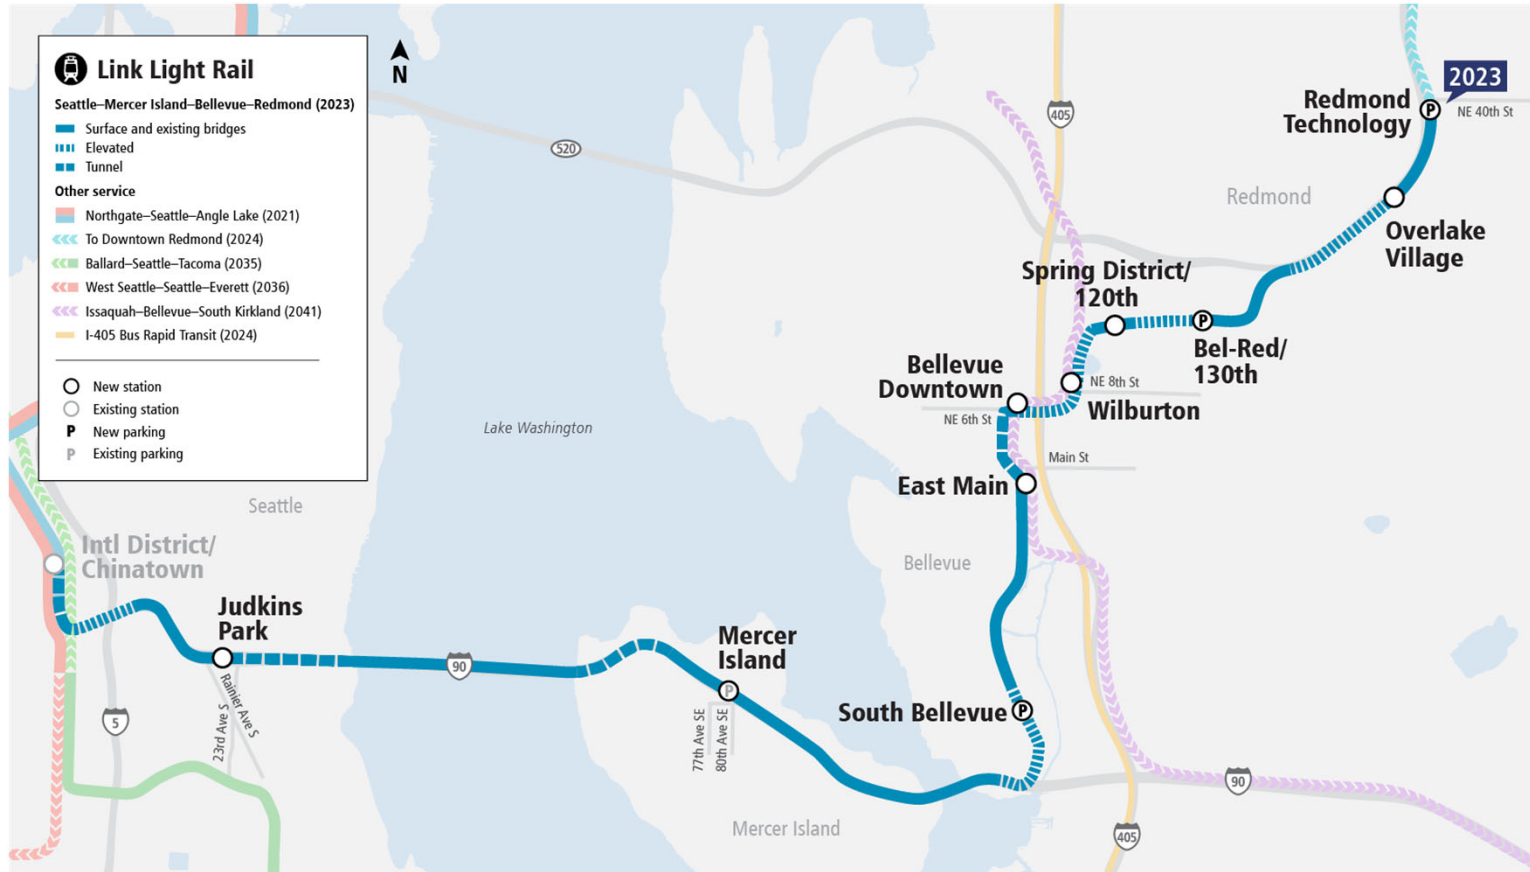

# *Why are we here*

## **Increase ST CMC (Jacobs) Contract by \$15,000,000**

E130 extended from Q4 2021 to Q4 2022


- a) Complexities of the Work
- b) Track Plinth Quality Issues
- c) COVID-19 Impacts
- d) Concrete Strike

***Motion No. M2022-22 – Contract Modification for East Link  
Extension I-90 Segment Construction Management Services***

Illustrative - Not to Scale

# EAST LINK EXTENSION: Baseline Budget \$3.68B


ALLOCATION \$ COMMITMENTS

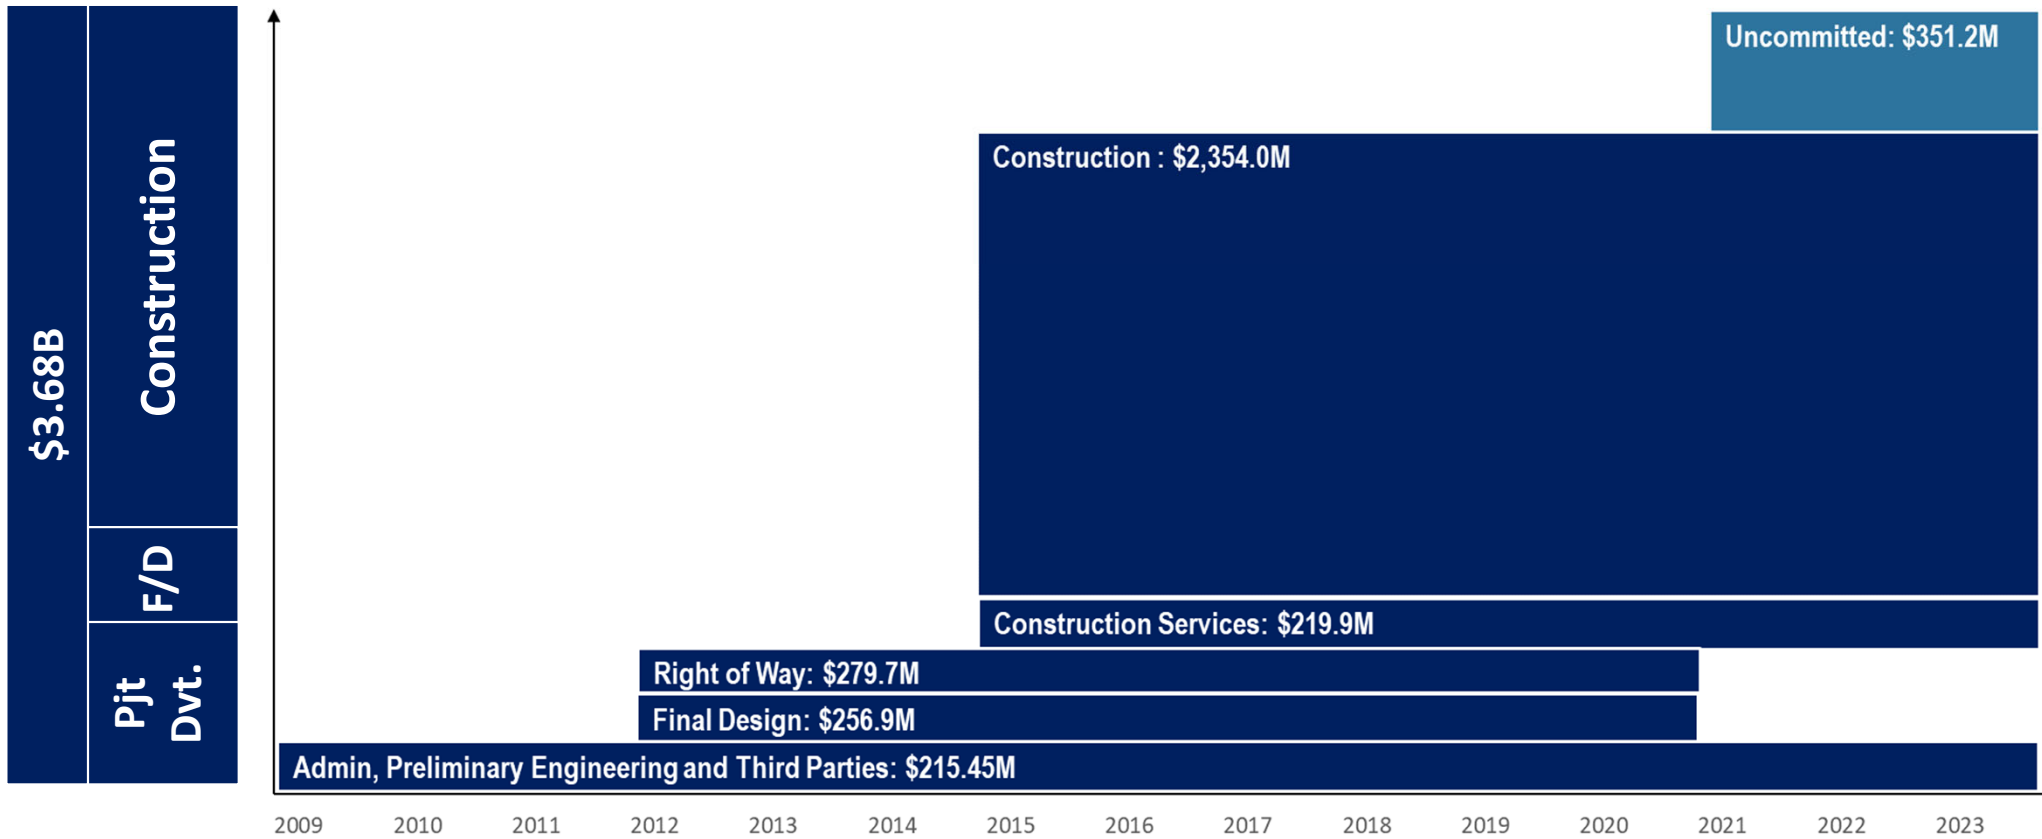

Illustrative - Not to Scale

# EAST LINK EXTENSION: Board Approves contract with Jacobs Project Management Company for \$15M in Construction Services

ALLOCATION \$ COMMITMENTS

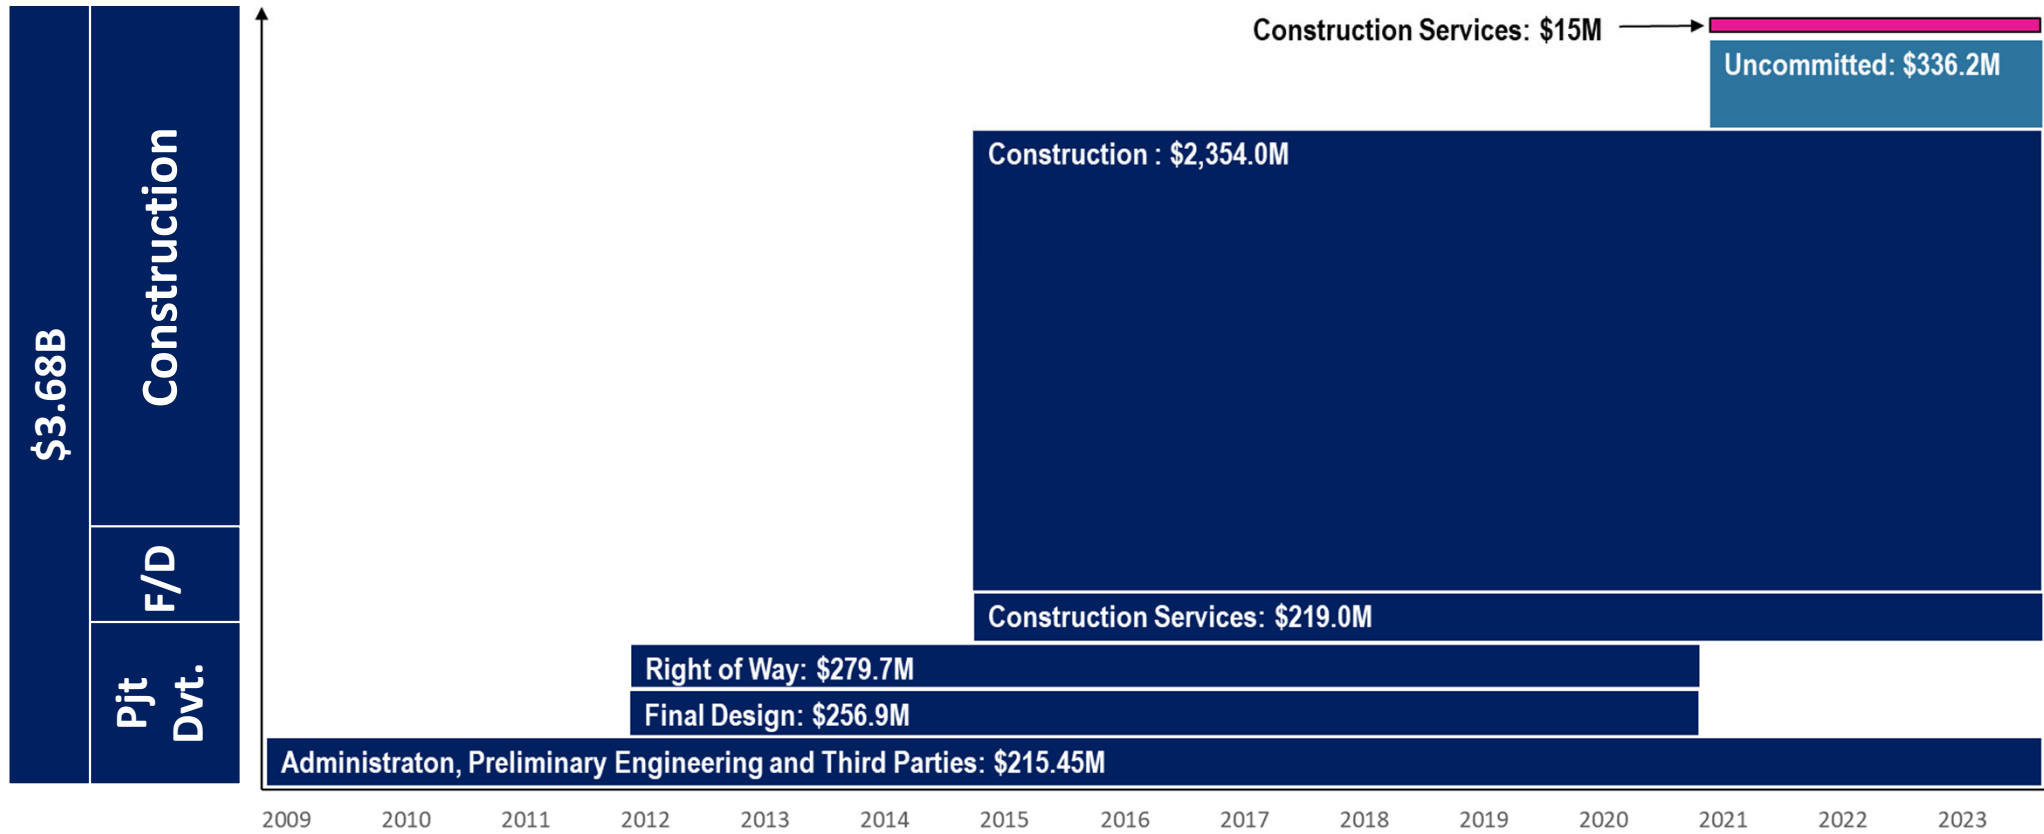

*Thank you.*



 [soundtransit.org](https://www.soundtransit.org)

