


next generation ORCA Monthly Program Dashboard

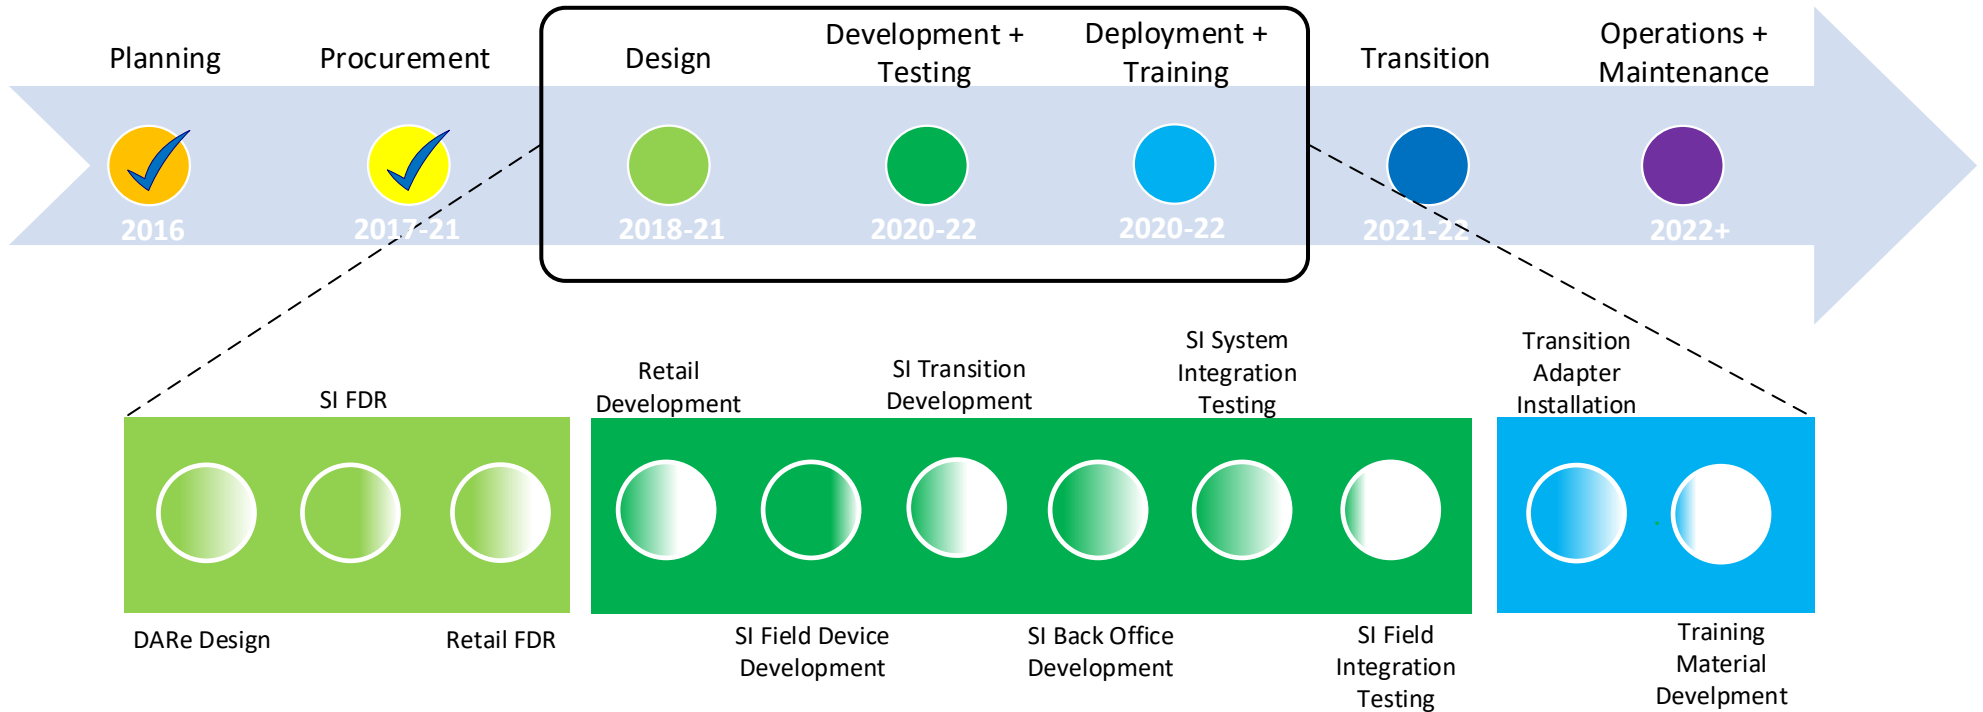

Actions Complete

(in last ~two months)

- SI Final Design Substantial Completion 5/26/21
- SI Preliminary Design Reviews Completed 6/4/21
- Agency Test Facility Installation Complete 6/11/21
- Production Environment Infrastructure Installed 7/9/21
- SI Field Integration Testing Started 7/9/21

Upcoming Actions Anticipated

(in next ~two months)

- First Pass of Phase II Project Ranking 7/16/21
- SI System Integration Testing Round 1 Complete 7/30/21
- DARe – Iteration 1 Reports Defined 7/30/21
- Transition Adapter Kit Deliveries Complete 8/31/21
- SI Transition Development Complete 9/3/21

Program Status

	Schedule (crit. path on track)
	Budget (within target)
	Risk (balanced, 23% high)

Legend

Symbol	Description
<input type="checkbox"/>	To do
<input checked="" type="checkbox"/>	Done
	Complete
	In progress
	Just completed
